Measuring Progress on Projects & Timelines

**Canada West Foundation** cwf.cq

**DECISION-MAKING** 

complete (Cedar LNG)

in process


Almost all projects are still in the early stages of the IA process

pre-planning

in process

Analysis of all projects from August, 2019 (when the IAA was enacted) through April, 2023

The Impact Assessment Agency of Canada (IAAC) has been amassing substantial experience in managing Phase 1 of the process. However, it hasn't gotten to the hard parts yet.

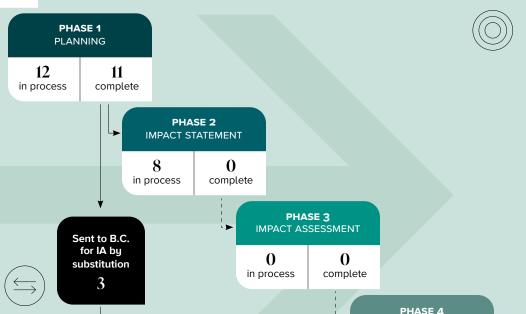

## On time for Phase 1? Depends how you count.



However, the total number of days proponents spent in Phase 1 was not 180, but an average of 332 (range of 127 to 693).

The near-complete failure to reach 180 days without stopping the clock indicates that the Planning phase is not working as intended. Substantial changes are clearly needed.

A CAVEAT: the Planning phase may still succeed in reducing the overall timeline of the IA process, but we won't know for several years.

\$1.3B in Budget 2023 to improve regulatory efficiency
